



# Brentwood Care Centre PHASE-3 IMPACT CALENDAR for Sept 3 – 16 / 2017

Sun	Monday	Tuesday	Wednesday	Thursday	Friday	Sat
Sept-3 W k 74	Sept-4 <i>P,A,C</i>  Labor Day	Sept-5 <i>P,A,C</i>  <ul style="list-style-type: none"> <li>➤ Set Up Hoarding &amp; Begin Finishing Office Beside Chris' Temp Office</li> <li>➤ Interior Construction inc 1F Drywall &amp; Partitions</li> <li>➤ Roof Construction</li> </ul>	Sept-6 <i>P,A,C</i>	Sept-7 <i>P,A,C</i>	Sept-8 <i>P,A,C</i>	Sept-9
Sept-10 W k 75	Sept-11 <i>P,A,C</i>	Sept-12 <i>P,A,C</i>	Sept-13 <i>P,A,C</i>	Sept-14 <i>P,A,C</i>	Sept-15 <i>P,A,C</i>	Sept-16
<ul style="list-style-type: none"> <li>➤ Finish Office Beside Chris' Temp Office</li> <li>➤ Interior Construction inc 1F Drywall &amp; Partitions</li> <li>➤ Exterior Finishes, EIFS</li> <li>➤ Roof Construction</li> <li>➤ RETAINING WALL &amp; SIDEWALK CONSTRUCTION – on east side of crane</li> </ul>						




## IMPACT EVENTS

- P* Parkade Access Disruptions
- A* Building Access Interruptions
- C* Construction Activity
- R* Resident Area Disruptions

- S* Staff Area Disruptions
- E* Planned Power Shut Down
- W* Planned Water Shut Down
- N* Excess Noise

August-October Surface Improvements Out Front Include: 1) removing the remaining Drive Aisle asphalt, 2) excavating for and installing the grade separation retaining wall near the front of the new building, 3) installing the new sidewalk near the front of the new building, 4) removing the Temp Entrance exterior platform/steps/ramp and providing relocated barrier free access to the Temp Entrance, 5) removing the crane in September, 6) installing the parkade ramp 7) finishing all front sidewalks and Drive Aisle new asphalt.

Intercare Has Assigned Responsibility For Traffic Management During Construction To Clark Builders. To Ensure The Safety & Security Of All Construction Personnel, Brentwood Staff & Visitors, Please Obey The Posted Signage And The Instructions & Directions Given By Clark Builders Traffic Management Personnel.

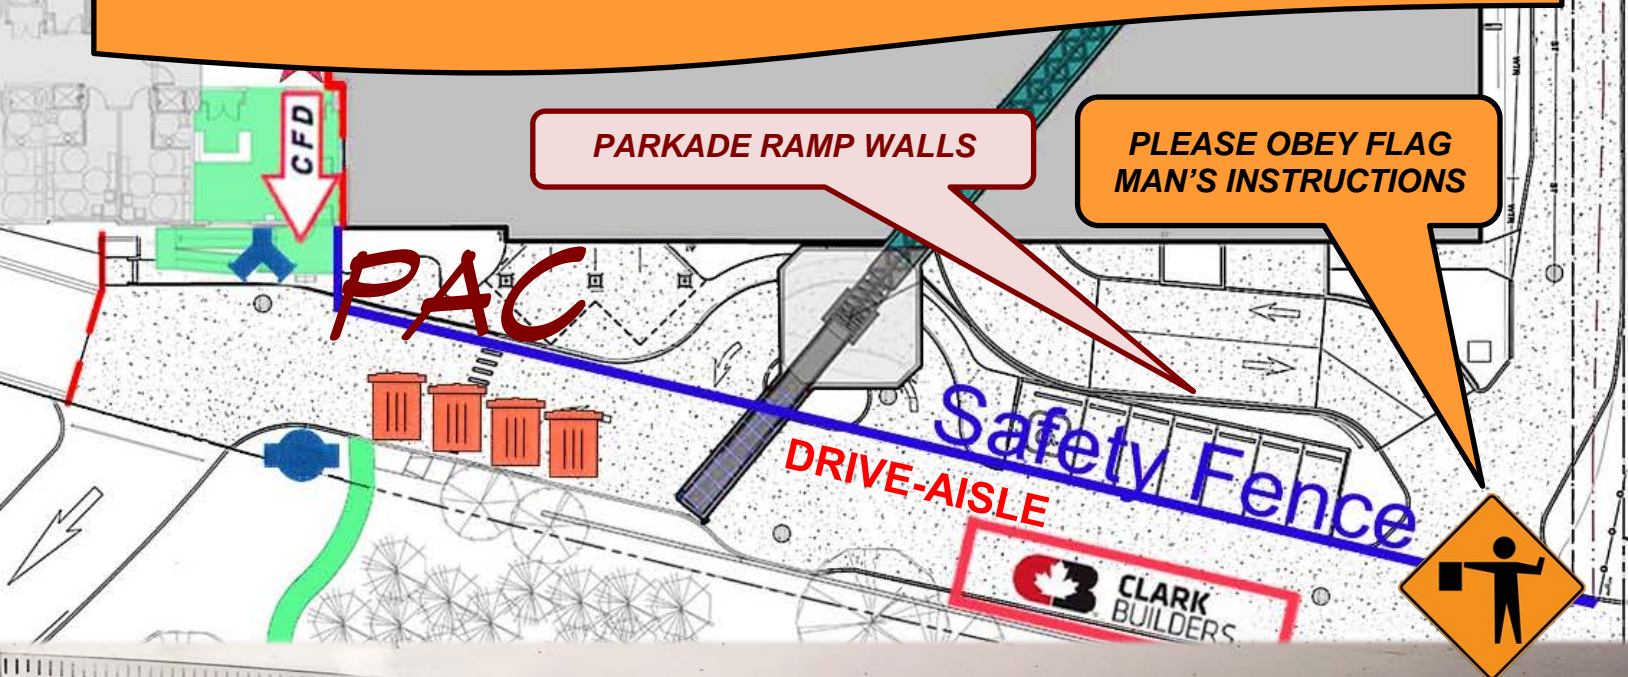

August-30

Main Floor South Side

Resident Room Ceiling Drywall & Partition Framing
